പതിമൂന്നാം കേരള നിയമസഭ പതിനൊന്നാം സമ്മേളനം

നക്ഷത്രചിഹ്നമിടാത്ത ചോദ്യം നമ്പർ: 4285 25.06.2014-ലെ മറുപടിയ്ക്ക്

കടലുകാണിപ്പാറ ടൂറിസം പദ്ധതിയുടെ നിർമ്മാണം

ചോദ്യം

ഉത്തരം

പകർപ്പ്

ശ്രീ.ബി.സത്യൻ

ശ്രീ.എ.പി.അനിൽകുമാർ (ബഹു. പട്ടികജാതി–പിന്നോക്ക സമുദായ ക്ഷേമവും വിനോദസഞ്ചാരവും വകുപ്പു മന്ത്രി)

- (എ) പുളിമാത്ത് കടലുകാണിപ്പാറ (എ) അന്വേഷണ റിപ്പോർട്ടിന്റെ പക ടൂറിസം പദ്ധതിയുടെ നിർമ്മാണ അനുബന്ധമായി ചേർത്തിരിക്കുന്നു. പ്രവർത്തനവുമായി ബന്ധപ്പെട്ട് ഉണ്ടായ പരാതിയിൻമേലുള്ള അന്വേഷണ റിപ്പോർട്ടിന്റെ പകർപ്പ് ലഭ്യമാക്കാമോ;
- (ബി) അനോഷണ റിപ്പോർട്ട് പരിശോധിച്ച് (ബി) അനോഷണ റിപ്പോർട്ട് പരിശോധിച്ച് എന്ത് നടപടിയാണ് ആവശ്യമായ നടപടികൾ സ്വീകരിച്ചിട്ടുള്ളതെന്ന് സ്വീകരിക്കുന്നതാണ്.

സെക്ഷൻ ഓഫീസർ

From

Blow 201 um.

Regional Joint Director Office Department of Tourism Norka Building Thycaud

To

Joint Director

The Director
Department of Tourism

Thiruvananthapuram Dated: 3-12-2013

Sir,

SÚB - JOINT SITE INS Kadalukanippara Tourism Project -Inspect repoort - reg

Ref:

1. Letter No. P2-5473/2010 dated 19/11/2013 from Director Tourism

2. G.O (MS) No.3996/12/TSM dated 16.05.2012

With reference to the letter 1st cited, we had jointly inspect the site along with Smt. Krishna kumari- Habitat, Mr. Biju site-in-charge-Habitat, Mr. Ebby Stalin, Project Engineer of this Department.

As per 2nd cited Government of Kerala accorded Administrative sanction for the project "Kadalukanippara Tourism Project" at an estimated cost of Rs.55,00,000/- with following components.

Se 010:	(September 1998) Protestina interes	
1	Viewing points – 2nos	4,40,000.00
2	Vehicle parking	5,40,000.00
3	Pavilions	2,10,000.00
4	Electrification works	9,40,000.00
5	Walkways	11,45,000.00
6	Protective fencing	5,80,000.00
7	Public Toilet	6,40,000.00
8	Landscaping and signages	3,70,000.00
9	Total	48,65,000.00
10	KVAT 3.03%	1,47,409.50
11	KCWWF 1.00%	48,650.00
12	Professional fee 8%	3,89,200.00
13	Service Tax 12.36% on fees	48,105.12
14	Grand Total	54,98,364.62
	Sanctioned Amount – Rupees Fifty Five Lakhs only	55,00,000.00


During the site inspection component wise measurement was taken by the Project Engineer and the components where found as per the detailed drawings submitted by the Executing Agency. As per the site measurements the executing agency was directed to submit the component wise expenditure incurred statement. But they have been done the work of landscaping is not up to the mark which an amount may be deducted. Further payment can only be released after getting the actual expenditure statement, UC & CC. The present pictures of the project components were also enclosed herewith.

Yours Faithfully


X

anosam s. slmh


Joint Directo



Protective Fencing near rock - 65m



Public Toilet with water tank, Septic & appx. 2000 litre sump for water storage

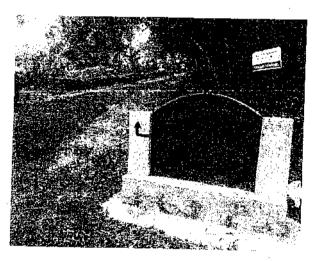

Signage




Landscaping

3/12/2013


Thiruvananthapuram

Joint Director

The present pictures of project components are as follows.




Viewing points – 2 nos



Vehicle Parking (27.6m x 3.5m)




Pavillions



Electrification works & Seating



Walkways



View point & Seating area

om alm os olmit.
